

番号:現場名	元 請	班 名	更新日	契約屯数	入荷屯数	出荷屯数	未入荷屯数	在庫屯数
1:ジェムビル	大森建設	池田鉄筋	12/01/25	1,224.820	1,198.100	79.434	26.720	1,118.667
2:上野台マンション	大森建設	船場鉄筋	12/01/25	816.463	460.675	419.534	355.788	41.142
3:池田町役場旧館建替工	大森建設	田中铁筋	12/01/25	839.517	485.543	230.561	353.974	254.982
4:山田地区集合住宅新築	小成組	田中铁筋	12/01/25	1,492.471	1,105.764	1,055.939	386.707	49.825
5:前川マンション新築	笹中工務店	山田鉄筋	12/01/25	225.600	228.964	227.533	- 3.364	1.431
6:株式会社ジェム本社	大森建設	箕面鉄筋	12/01/25	918.521	130.859	99.598	787.662	31.262
7:新大阪ビル新築	大森建設	田中铁筋	00/09/30		209.473	130.317		79.156
8:山田地区集合住宅新築	小成組	田中铁筋	12/01/25		1,020.822	1,056.124		- 35.302
9:津野歯科医院	小成組	田中铁筋	00/03/27	261.549	243.166	254.956	18.383	- 11.790
10:新御堂池田ビル	笹中工務店	山田鉄筋	00/04/24	79.009	78.977	84.431	0.032	- 5.454
11:箕面千里ハイツ	小成組	池田鉄筋	10/07/02		353.738	342.352		11.386
12:ジェムビル付帯施設工	笹中工務店	田中铁筋	12/01/25	1,501.261	915.298	892.529	585.963	22.769
13:上新田醍醐マンション	小成組	田中铁筋	11/04/08	0.131	413.624	0.025	- 413.493	413.599
14:大阪山田賢マンション	小成組	船場鉄筋	12/01/25	277.412	281.362	310.559	- 3.950	- 29.198
15:谷町興産第5ビル	小成組	船場鉄筋	00/03/22	40.993	40.979	38.682	0.014	2.296
16:石橋ハイツ	小成組	船場鉄筋	05/04/11		200.652	180.842		19.810
17:山田電気(株)本社ビル	小成組	田中铁筋	00/10/02		557.519	580.946		- 23.427
18:物流総合共同施設	竹水建設	船場鉄筋	11/10/19		297.963	107.796		190.167
19:穴胡ブロード新築工事	小成組	池田鉄筋	12/01/25		428.571	221.469		207.102
20:キャッスルハイツ箕面船場	小成組	田中铁筋	04/11/13		33.049	102.576		- 69.527
総合計				7,677.747	8,685.099	6,416.202	2,094.435	2,268.895

工事名：ジェムビル新築工事










総重量 13,786kg

規格	SD295A	SD295A	SD295A	SD345	SD345	SD345	SD345	SD390	SD390	SD390	SD390	SD390
径	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
3.5m	15	11	11	4	10	25						
4.0m	6	26	15	22	35	24						
4.5m	33	31	40	13	11	33						
5.0m	46	23	44	32	30	145						
5.5m	23	61		35		65						
6.0m	54	23		61		80						
6.5m	34	46	33									
7.0m		32										
7.5m												
8.0m												
8.5m												
9.0m												
9.5m												
10.0m												
10.5m												
11.0m												
11.5m												
12.0m												
重量	13,786	631	1,386	1,111	1,977	1,140	7,541	0	0	0	0	0

12: ジェムビル付帯施設工
1 -1階 壁 F-B1F. 壁

[元請: 清水建設
[班: 山田

] 加工日: 12年 6月10日
] 出荷日: 12年 6月10日

番号	径	材種	形状	長さ	本数	倍数	
1	D13	SD295A	150 	4,500	17	1	
2	D13	SD295A	150 	3,500	17	1	
3	D13	SD295A	150 	3,250	17	1	
4	D13	SD295A	150 	4,000	17	1	
5	D13	SD295A	 4080	4,230	29	1	
6	D13	SD295A		3,750	29	1	
7	D13	SD295A		3,200	2	1	
8	D13	SD295A	150 	5,000	34	1	
9	D13	SD295A	150 	5,500	17	1	
10	D13	SD295A	150 	4,500	17	1	
11	D13	SD295A	 4120	4,270	40	1	
12	D13	SD295A		3,800	40	1	
13	D13	SD295A		3,240	2	1	
14	D13	SD295A	150 	4,000	4	1	
15	D13	SD295A	150 	3,500	4	1	
16	D13	SD295A		3,500	4	1	
17	D13	SD295A		4,000	4	1	
18	D13	SD295A	170  4200	4,500	28	1	
19	D13	SD295A	170  740 150	1,170	14	1	
20	D13	SD295A	170  460 150	890	14	1	
21	D13	SD295A	 4200	4,350	19	1	
22	D13	SD295A		3,850	19	1	
23	D13	SD295A	 1350	1,500	9	1	
24	D13	SD295A	200  1350	1,650	9	1	
25	D16	SD295A	 4120	4,270	2	1	

D16: 13kg D13: 1558kg

実寸重量 1,571 kg

番号	現場名	元請	班名	契約重量	入荷重量	出荷重量
1	ジェムビル		佐藤	369,650	134,947	73,737
工事期間 平成 22年 7月 2日～平成 22年 7月 2日 締切日 毎月 日 ～ 翌月 日						

番号	年月日	箇所名	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
1	10/07/02	0F 基礎 A工区 Y1通	13,914	236	3,478	7,839		2,361							
2	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
3	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
4	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
5	10/07/02	0F 基礎	9,172	236	3,478	817		2,361			2,280				
6	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
7	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
8	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
9	10/07/02	0F 基礎	6,892	236	3,478	817		2,361							
10	10/07/02	5F 小梁	1,195						1,195						
11	10/07/02	6F 小梁	504							504					
12	10/07/02	12F 梁 A工区 Y1通	707			513	194								

			合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
		契約重量	369,650	15,400	27,350	42,900	62,000	83,500		138,500					
		入荷重量	134,947	10,570	94,300	14,214	1,805			339	13,720				
		出荷重量	73,737	2,127	31,298	14,888	194	21,251	1,195	504	2,280				

平成 22年 7月 2日	伝票番号:部位	摘要	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
1:ジェムビル	3:		94,300	0	94,300	0	0	0	0	0	0	0	0	0	0
1:ジェムビル	4:		-312,923	0	0	14,214	1,805	0	0	339	-329,280	0	0	0	0
2:上野台マンション	1:	岸鉄	5,970	0	5,970	0	0	0	0	0	0	0	0	0	0
2:上野台マンション	2:	岸鉄	6,567	0	6,567	0	0	0	0	0	0	0	0	0	0
11:箕面千里ハイツ	1:	神鉄	7,283	0	7,283	0	0	0	0	0	0	0	0	0	0
12:ジェムビル付帯施設工	1:	合鉄	5,060	0	0	0	0	5,060	0	0	0	0	0	0	0
12:ジェムビル付帯施設工	2:	合鉄	5,496	0	0	0	0	0	5,496	0	0	0	0	0	0
		7月 2日 入荷合計	-188,247	0	114,120	14,214	1,805	5,060	5,496	339	-329,280	0	0	0	0
1:ジェムビル	2: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	3: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	4: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	5: 0階	基礎	9,172	236	3,478	817	0	2,361	0	0	2,280	0	0	0	0
1:ジェムビル	6: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	7: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	8: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	9: 0階	基礎	6,892	236	3,478	817	0	2,361	0	0	0	0	0	0	0
1:ジェムビル	10: 5階	小梁	1,195	0	0	0	0	0	1,195	0	0	0	0	0	0
1:ジェムビル	11: 6階	小梁	504	0	0	0	0	0	0	504	0	0	0	0	0
1:ジェムビル	12: 12階	梁 A工区 Y1通	707	0	0	513	194	0	0	0	0	0	0	0	0
4:新箕面市役所仮庁舎	1: 1階	梁 1-1G,増打	3,901	0	0	0	0	0	3,901	0	0	0	0	0	0
4:新箕面市役所仮庁舎	2: 1階	梁 1-1G,増打	2,377	36	0	1,079	111	255	896	0	0	0	0	0	0
4:新箕面市役所仮庁舎	3: 1階	梁 1-1G,増打	5,058	1,364	3,694	0	0	0	0	0	0	0	0	0	0
5:前川マンション新築	59: 3階	壁 3W	954	241	712	0	0	0	0	0	0	0	0	0	0
5:前川マンション新築	60: 4階	梁 4G	5,510	27	325	100	0	636	4,421	0	0	0	0	0	0
8:山田地区集合住宅新築307:	6階	壁 北3工区. 6W6	1,203	463	651	89	0	0	0	0	0	0	0	0	0
8:山田地区集合住宅新築308:	6階	壁 北3工区. 6W6	3	0	3	0	0	0	0	0	0	0	0	0	0
8:山田地区集合住宅新築309:	7階	梁 南棟1工区. 7G(地組)	5,870	35	0	119	0	0	179	5,536	0	0	0	0	0
11:箕面千里ハイツ	1: 0階	基礎 1工区. F	8,040	0	940	145	0	4,729	2,226	0	0	0	0	0	0
11:箕面千里ハイツ	2: 0階	柱 1工区. FC(7-ブ)	3,742	0	3,742	0	0	0	0	0	0	0	0	0	0
11:箕面千里ハイツ	3: 0階	基礎梁 1工区. F..	2,049	0	0	320	0	547	1,183	0	0	0	0	0	0
11:箕面千里ハイツ	4: 0階	基礎梁 1工区. F..	392	0	392	0	0	0	0	0	0	0	0	0	0
11:箕面千里ハイツ	5: 0階	基礎梁 1工区. FG	9,367	77	104	2,950	0	0	0	265	0	5,971	0	0	0
12:ジェムビル付帯施設工	1: 0階		0	0	0	0	0	0	0	0	0	0	0	0	0
12:ジェムビル付帯施設工	2: 0階	雑 カンザシ	56	56	0	0	0	0	0	0	0	0	0	0	0
12:ジェムビル付帯施設工	3: 0階	雑 カンザシ	140	140	0	0	0	0	0	0	0	0	0	0	0
12:ジェムビル付帯施設工	4: -3階	床版 A-B3F. FS下筋	15,618	439	1,194	13,985	0	0	0	0	0	0	0	0	0
		7月 2日 定尺合計	124,104	4,770	39,579	25,836	305	25,056	14,002	6,305	2,280	5,971	0	0	0

細物: D10~D13 太物: D16~D51

材種: 全部

全現場

平成 22年 7月 2日	伝票番号:部位	摘要	総合計 A+B	細物生材	太物生材	生材合計 A	細物曲げ	太物曲げ	曲げ合計①	細物切断	太物切断	切断合計②	細物切曲	太物切曲	切曲合計③	①+②+③ B
	1: ジェムビル	1: 0階 基礎 A工区 Y1通	13,914	0	7,022	7,022	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	2: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	3: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	4: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	5: 0階 基礎	9,172	0	2,280	2,280	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	6: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	7: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	8: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	9: 0階 基礎	6,892	0	0	0	808	2,361	3,169	0	0	0	2,906	817	3,723	6,892
	1: ジェムビル	10: 5階 小梁	1,195	0	0	0	0	1,195	1,195	0	0	0	0	0	0	1,195
	1: ジェムビル	11: 6階 小梁	504	0	0	0	0	504	504	0	0	0	0	0	0	504
	1: ジェムビル	12: 12階 梁 A工区 Y1通	707	0	219	219	0	488	488	0	0	0	0	0	0	488
	4: 新箕面市役所仮庁舎	1: 1階 梁 1-1G, 増打	3,901	0	681	681	0	1,639	1,639	0	0	0	0	1,580	1,580	3,220
	4: 新箕面市役所仮庁舎	2: 1階 梁 1-1G, 増打	2,377	0	480	480	0	564	564	36	85	121	0	1,213	1,213	1,897
	4: 新箕面市役所仮庁舎	3: 1階 梁 1-1G, 増打	5,058	561	0	561	0	0	0	9	0	9	4,488	0	4,488	4,497
	5: 前川マンション新築	59: 3階 壁 3W	954	0	0	0	17	0	17	0	0	0	936	0	936	954
	5: 前川マンション新築	60: 4階 梁 4G	5,510	211	1,263	1,475	0	2,105	2,105	0	0	0	141	1,789	1,930	4,035
	6: 株式会社ジェム本社	6: 0階 基礎梁 FG (STR) 追加	30	0	0	0	0	0	0	0	0	0	30	0	30	30
	6: 株式会社ジェム本社	27: 2階 床版 2S	1,586	778	0	778	426	0	426	262	0	262	120	0	120	808
	6: 株式会社ジェム本社	28: 3階 床版 3S	1,586	778	0	778	426	0	426	262	0	262	120	0	120	808
	6: 株式会社ジェム本社	29: 4階 床版 4S	1,586	778	0	778	426	0	426	262	0	262	120	0	120	808
	6: 株式会社ジェム本社	30: 5階 床版 5S	1,586	778	0	778	426	0	426	262	0	262	120	0	120	808
	6: 株式会社ジェム本社	31: 6階 床版 6S	1,586	778	0	778	426	0	426	262	0	262	120	0	120	808
	6: 株式会社ジェム本社	32: 2階 床版 2 F. 開口スリーブ	482	0	0	0	0	0	0	482	0	482	0	0	0	482
	6: 株式会社ジェム本社	33: 3階 床版 3 F. 開口スリーブ	482	0	0	0	0	0	0	482	0	482	0	0	0	482
	6: 株式会社ジェム本社	34: 4階 床版 4 F. 開口スリーブ	482	0	0	0	0	0	0	482	0	482	0	0	0	482
	6: 株式会社ジェム本社	35: 5階 床版 5 F. 開口スリーブ	482	0	0	0	0	0	0	482	0	482	0	0	0	482
	8: 山田地区集合住宅新築307	6階 壁 北3工区. 6W6	1,203	118	11	129	426	0	426	251	78	329	319	0	319	1,074
	8: 山田地区集合住宅新築308	6階 壁 北3工区. 6W6	3	0	0	0	0	0	0	3	0	3	0	0	0	3
	8: 山田地区集合住宅新築309	7階 梁 南棟1工区. 7G (地組)	5,870	0	3,269	3,269	0	2,253	2,253	0	0	0	35	313	349	2,601
	11: 箕面千里ハイツ	1: 0階 基礎 1工区. F	8,040	0	0	0	0	0	0	0	145	145	940	6,955	7,895	8,040
	11: 箕面千里ハイツ	2: 0階 柱 1工区. FC (7-7)	3,742	0	0	0	0	0	0	0	0	0	3,742	0	3,742	3,742
	11: 箕面千里ハイツ	3: 0階 基礎梁 1工区. F..	2,049	0	0	0	0	0	0	0	39	39	0	2,010	2,010	2,049
	11: 箕面千里ハイツ	4: 0階 基礎梁 1工区. F..	392	0	0	0	146	0	146	20	0	20	226	0	226	392
	11: 箕面千里ハイツ	5: 0階 基礎梁 1工区. FG	9,367	104	721	825	0	5,533	5,533	0	0	0	77	2,932	3,009	8,542
		7月 2日 出荷合計	132,088	4,881	15,946	20,827	9,992	35,531	45,523	3,554	347	3,901	37,691	24,146	61,837	111,261

8 山田地区集合住宅新築			小成建設												
出荷日	部位		合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
307:10/07/02	6F 壁	北3工区. 6W6	1,203	463	651	89									
308:10/07/02	6F 壁	北3工区. 6W6	3		3										
309:10/07/02	7F 梁	南棟I工区. 7G(地組)	5,870	35		119			179	5,536					
	合計		7,076	498	655	208			179	5,536					

12 ジェムビル付帯施設工			静水建設												
出荷日	部位		合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
2:10/07/02	0F 雑	カンザシ	56	56											
3:10/07/02	0F 雑	カンザシ	140	140											
4:10/07/02	-3F 床版	A-B3F. FS下筋	15,618	439	1,194	13,985									
	合計		15,814	635	1,194	13,985									

山田			合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
8	山田地区集合住宅新築		7,076	498	655	208			179	5,536					
12	ジェムビル付帯施設工		15,814	635	1,194	13,985									
	合計		22,891	1,133	1,849	14,193			179	5,536					

4 新箕面市役所仮庁舎 田中

出荷日	部位	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
1:10/07/02	1F 梁 1-1G,増打	3,901						3,901						
2:10/07/02	1F 梁 1-1G,増打	2,377	36		1,079	111	255	896						
3:10/07/02	1F 梁 1-1G,増打	5,058	1,364	3,694										
	合計	11,336	1,401	3,694	1,079	111	255	4,797						

8 山田地区集合住宅新築 山田

出荷日	部位	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
307:10/07/02	6F 壁 北3工区. 6W6	1,203	463	651	89									
308:10/07/02	6F 壁 北3工区. 6W6	3		3										
309:10/07/02	7F 梁 南棟1工区. 7G(地組)	5,870	35		119			179	5,536					
	合計	7,076	498	655	208			179	5,536					

11 箕面千里ハイツ 池田

出荷日	部位	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
1:10/07/02	0F 基礎 1工区. F	8,040		940	145		4,729	2,226						
2:10/07/02	0F 柱 1工区. FC(7-7)	3,742		3,742										
3:10/07/02	0F 基礎梁 1工区. F.	2,049			320		547	1,183						
4:10/07/02	0F 基礎梁 1工区. F.	392		392										
5:10/07/02	0F 基礎梁 1工区. FG	9,367	77	104	2,950				265		5,971			
	合計	23,591	77	5,178	3,415		5,275	3,409	265		5,971			

小成建設

	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
4 新箕面市役所仮庁舎	11,336	1,401	3,694	1,079	111	255	4,797						
8 山田地区集合住宅新築	7,076	498	655	208			179	5,536					
11 箕面千里ハイツ	23,591	77	5,178	3,415		5,275	3,409	265		5,971			
合計	42,003	1,976	9,526	4,702	111	5,530	8,385	5,801		5,971			

12: ジェムビル付帯施設工 (単位: 本, kg)
 No.210 -1階 壁 F-B1F. 壁

[元請: 清水建設
 [班: 山田]

加工日: 12年 6月10日
 出荷日: 12年 6月10日

番号	径	材種	形状	長さ	本数	径	寸法	本数	重量
1	D13	SD295A	┌ 4120	4,270	40	D13	4.5	40	179
2	D13	SD295A	┌ 4080	4,230	36	D13	4.5	36	161
3	D13	SD295A	┌ 3960	4,110	8	D13	4.5	8	36
4	D13	SD295A	┌ 3850	4,000	28	D13	4.0	28	111
5	D13	SD295A	┌ 3240	3,390	38	D13	3.5	38	132
6	D13	SD295A	┌ 3210	3,360	28	D13	3.5	28	97
7	D13	SD295A	┌ 2980	3,130	10	D13	6.5	5	32
8	D13	SD295A	┌ 2680	2,830	9	D13	6.0	5	30
9	D13	SD295A	┌ 2380	2,530	9	D13	5.5	5	27
10	D13	SD295A	┌ 2300	2,450	28	D13	5.0	14	70
11	D13	SD295A	┌ 1350	1,500	9	D13	4.5	3	13
12	D13	SD295A	————	4,750	14	D13	5.0	14	70
13	D13	SD295A	————	4,550	14	D13	5.0	14	70
14	D13	SD295A	————	4,250	16	D13	4.5	16	72
15	D13	SD295A	————	4,000	28	D13	4.0	28	111
16	D13	SD295A	————	3,950	7	D13	4.0	7	28
17	D13	SD295A	————	3,850	26	D13	4.0	26	103
18	D13	SD295A	————	3,800	40	D13	4.0	40	159
19	D13	SD295A	————	3,750	36	D13	4.0	36	143
20	D13	SD295A	————	3,630	7	D13	4.0	7	28
21	D13	SD295A	————	3,500	48	D13	3.5	48	167
22	D13	SD295A	————	3,470	1	D13	3.5	1	3
23	D13	SD295A	————	3,350	1	D13	3.5	1	3
24	D13	SD295A	————	3,240	2	D13	6.5	1	6
25	D13	SD295A	————	3,200	2	D13	6.5	1	6

D13: 1781kg

実寸重量

1,781 kg

出荷本数一覧

(単位: 本, kg)

平成 22年 8月 6日

	D10	D13	D16	D16	D19	D22	D25	D29	D32
材種	SD295A	SD295A	SD295A	SD345	SD345	SD345	SD345	SD390	SD390
メーカー	岸鉄	岸鉄	岸鉄	合鉄	合鉄	合鉄	合鉄	神製	神製
3.5m	18	3,420	54	182		3,260	32	234	22
4.0m	261	180	44	32			35		
4.5m	342	297		486			36		
5.0m	135	918	34	109		324	46	243	8
5.5m	9	1,773		32	8	684	56		
6.0m		632	56	36	7	1,072	73	332	
6.5m	45	234		255		3,400		625	6
7.0m				32					30
7.5m	18	1,084	484	72					
8.0m									
8.5m									
9.0m									
9.5m									
10.0m									
10.5m									
11.0m									
11.5m									
12.0m									
出荷重量 247,083	2,127	41,592	7,022	9,834	194	137,734	5,532	40,768	2,280
出荷実重 245,712	2,025	40,513	7,022	9,644	194	137,734	5,532	40,768	2,280

出荷本数一覧
(単位: 本, kg)

平成22年 8月 6日

元請: 静水建設
班名: 山田

12: ジェムビル付帯施設工
伝票番号 1-250

	合計	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
定尺重量	893,184	32,128	261,375	213,068	102,953	34,107	81,604	167,950	0	0	0	0	0
実寸重量	881,997	31,771	256,531	211,200	101,390	33,755	80,632	166,719	0	0	0	0	0

◆生材→出荷◆

	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
3.5m	210	5128	1518	24	244	90	59					
4.0m	285	4109	3803	235	20	448	110					
4.5m	390	3646	486	438	288	280	1945					
5.0m	172	750	798	300	648	218	474					
5.5m	103	1347	325	113	4	24	1103					
6.0m	635	2800	56	125	62	100	31					
6.5m	1192	2055	4198	221	10	566	648					
7.0m	34	46	15	388		40	283					
7.5m		1012		356		16	90					
8.0m				410		37	48					
8.5m						6	151					
9.0m							9					
9.5m												
10.0m												
10.5m												
11.0m												
11.5m												
12.0m												
重量	(108)	(234)	(102)	(49)	(25)	(86)	(78)	(0)	(0)	(0)	(0)	(0)
423,005	9,437	99,518	87,531	35,930	18,019	38,272	134,298	0	0	0	0	0

◆切断→出荷◆

	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
3.5m	547	1712	1870	285		81	3					
4.0m	2724	1561	27	168		180	70					
4.5m	1519	807	44	65		97	75					
5.0m	439	596	87	146		68	618					
5.5m	41	541	119	7	40	150	9					
6.0m	420	2854	95	164		20	18					
6.5m	48	551	11	226	70	137						
7.0m	3	13	14			31	8					
7.5m							10					
8.0m							10					
8.5m												
9.0m												
9.5m												
10.0m												
10.5m												
11.0m												
11.5m												
12.0m												
重量	(163)	(288)	(60)	(61)	(7)	(113)	(40)	(0)	(0)	(0)	(0)	(0)
119,459	13,955	42,407	13,540	11,650	2,054	15,254	20,599	0	0	0	0	0
実寸重量	116,537	13,854	41,631	13,286	11,409	1,907	14,701	19,749	0	0	0	0

◆生材→曲げ→出荷◆

	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
3.5m	129	3378	68	21	44	279	35					
4.0m	109	652	118	848	36	133	42					
4.5m	174	1030	4362	235	65	128	35					
5.0m	35	81	4263	891	71	51	24					
5.5m	48	59	36	162	22	67	37					
6.0m	79	16	36	1	18	109	49					
6.5m	6	20	32	29	12	54	36					
7.0m	10	24	4		6	15						
7.5m	81	203		197	2	45						
8.0m						14						
8.5m												
9.0m												
9.5m												
10.0m												
10.5m												
11.0m												
11.5m												
12.0m												
重量	(55)	(119)	(76)	(56)	(56)	(145)	(19)	(0)	(0)	(0)	(0)	(0)
142,868	1,848	21,597	65,993	25,925	3,981	16,975	6,549	0	0	0	0	0

◆切断→曲げ→出荷◆

	D10	D13	D16	D19	D22	D25	D29	D32	D35	D38	D41	D51
3.5m	405	1568	75	142	12	27	5					
4.0m	616	5217	131	241	228	98	251					
4.5m	346	4041	780	655	61	108						
5.0m	161	2045	898	990	347	75	27					
5.5m	324	2734	2515	344	28	70	12					
6.0m	237	1852	357	52	25	124	11					
6.5m	287	1941	606	235	2	13						
7.0m	141	686	82		1	24						
7.5m						6						
8.0m			29		1	2						
8.5m				3	1							
9.0m												
9.5m												
10.0m												
10.5m												
11.0m												
11.5m												
12.0m												
重量	(257)	(863)	(145)	(241)	(67)	(177)	(14)	(0)	(0)	(0)	(0)	(0)
207,852	6,888	97,852	46,004	29,447	10,052	11,104	6,503	0	0	0	0	0
実寸重量	199,587	6,631	93,784	44,390	28,126	9,848	10,686	6,123	0	0	0	0

1:ジェムビル

受領書

伝票No.1

[元請:大森組

] 加工日:22年 6月20日

0階 基礎

A工区

Y1通

班:池田

出荷日:22年 7月 2日

No.	径	材種	形状	長さ	本数	径	寸法	本数	重量
1	D22	SD345 合鉄	250	6,000	60	D22	6.0	60	1,092
2	D22	SD345 合鉄	250	5,500	76	D22	5.5	76	1,269
3	D16	SD345 合鉄	1920	2,270	9	D16	7.0	3	33
4	D16	SD345 合鉄	1850	2,200	72	D16	4.5	36	253
5	D16	SD345 合鉄	1700	2,100	10	D16	4.5	5	35
6	D16	SD345 合鉄	1450	1,800	32	D16	7.5	8	94
7	D16	SD345 合鉄	1250	1,600	112	D16	6.5	28	283
8	D16	SD345 合鉄	1750	2,850	8	D16	6.0	4	37
9	D16	SD345 合鉄	1600	2,720	1	D16	3.5	1	5
10	D16	SD345 合鉄	1350	2,500	4	D16	5.0	2	16
11	D16	SD345 合鉄	1150	2,250	16	D16	4.5	8	56
12	D16	SD345 合鉄	2940	1,820	1	D16	3.5	1	5
13	D13	SD295A 岸鉄	620	820	90	D13	5.0	15	75
14	D13	SD295A 岸鉄	620	2,630	120	D13	5.5	60	328
15	D13	SD295A 岸鉄	450	3,630	84	D13	7.5	42	313
16	D13	SD295A 岸鉄	420	1,830	60	D13	5.5	20	109
17	D13	SD295A 岸鉄	320	1,630	15	D13	5.0	5	25
18	D13	SD295A 岸鉄	300	3,350	242	D13	3.5	242	842
19	D13	SD295A 岸鉄	300	2,550	234	D13	5.5	117	640
20	D13	SD295A 岸鉄	1350	5,000	56	D13	5.0	56	279
21	D13	SD295A 岸鉄	1350	4,500	24	D13	4.5	24	108
22	D13	SD295A 岸鉄	950	4,170	7	D13	4.5	7	31
23	D13	SD295A 岸鉄	950	4,000	8	D13	4.0	8	32
24	D13	SD295A 岸鉄	950	3,500	112	D13	3.5	112	390
25	D13	SD295A 岸鉄	600	2,470	4	D13	5.0	2	10
26	D13	SD295A 岸鉄	600	2,400	48	D13	5.0	24	120
27	D13	SD295A 岸鉄	600	2,250	4	D13	4.5	2	9

28	D13	SD295A 岸鉄	600	2,000	24	D13	4.0	12	48
29	D13	SD295A 岸鉄	600	1,800	64	D13	7.5	16	119
30	D10	SD295A 岸鉄	100	300	18	D10	5.5	1	3
31	D10	SD295A 岸鉄	450	640	24	D10	4.0	4	9
32	D10	SD295A 岸鉄	300	500	200	D10	4.0	25	56
33	D10	SD295A 岸鉄	250	450	1	D10	3.5	1	2
34	D10	SD295A 岸鉄	200	400	3	D10	3.5	1	2
35	D10	SD295A 岸鉄	250	900	30	D10	5.0	15	42
36	D10	SD295A 岸鉄	250	600	8	D10	7.5	2	8
37	D10	SD295A 岸鉄	200	500	20	D10	6.5	5	18
38	D10	SD295A 岸鉄	200	450	46	D10	4.5	16	40
39	D10	SD295A 岸鉄	100	400	86	D10	4.5	22	55
40	D16	SD295A 岸鉄		3,500	33	D16	3.5	33	180
41	D16	SD295A 岸鉄		3,500	21	D16	3.5	21	115
42	D16	SD295A 岸鉄		4,000	44	D16	4.0	44	275
43	D16	SD295A 岸鉄		6,000	56	D16	6.0	56	524
44	D16	SD295A 岸鉄		7,500	123	D16	7.5	123	1,439
45	D16	SD295A 岸鉄		7,500	361	D16	7.5	361	4,224
46	D16	SD295A 岸鉄		5,000	34	D16	5.0	34	265
47									
48									
49									
50									
D22	2361kg	D16	7839kg	D13	3478kg	D10	236kg		
									定尺重量 13,914kg

印	
---	--

入荷日	備考	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
10:99/12/01		7,834		7,834										
11:99/12/02		2,088		2,088										
12:99/12/02		19,063	7,392	11,671										

出荷日	箇所名	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
8:99/12/06	-1F 柱 B1F-C.W.物件	7,051	29	1,557	3,768		38	1,658						
9:99/12/08	0F 基礎 F.FC(5-8工区)	3,501		602	509			2,390						
10:99/12/08	1F 基礎梁 FG(6-8工区)	9,549	67	2,561				2,571	4,350					
12:99/12/08	0F 基礎梁 FG変更追加	733							733					
15:99/12/09	0F 雑 雑 追加	49					49							
13:99/12/13	1F 基礎 八カ.他.増打.ハキ	4,215		2,818	1,398									
14:99/12/13	0F 基礎 八カ.他.増打.ハキ	413	327	86										
16:99/12/13	1F 壁 5-8工区.1F.ハキ	2,195	179	2,016										
11:99/12/14	1F 梁 1G(4-6工区)	3,994	73	707		58		3,155						
17:99/12/14	1F 階段 4.5-工区.1K	196	72	124										
18:99/12/21	1F 床版 4-5工区.1S	1,922	34	1,889										
19:99/12/21	1F 床版 4.5工区-1S追加	594	87	204	303									
20:99/12/21	1F 壁 1F.ハキ追加	224		224										

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
繰越	51,902	7,383	18,653	7,949	509	617	12,330	4,462					
入荷	28,985	7,392	21,593										
出荷	34,635	868	12,787	5,978	58	87	9,774	5,083					
繰越	46,252	13,907	27,459	1,971	450	530	2,556	-621					
入荷累計	93,993	14,826	42,947	12,698	900	728	17,433	4,462					
出荷累計	47,742	919	15,488	10,727	450	198	14,877	5,083					
在庫累計	46,252	13,907	27,459	1,971	450	530	2,556	-621					

[合計]

ジェムビル付帯施設工

階部材別・出荷重量一覧表

(単位 : kg)

平成 22年 8月 6日

階	基礎	柱	壁	基礎梁	基礎小梁	梁	小梁	床版	階段	雑	合計
-3	7,143	36,869	36,243	309,765	42,986	270	12,561	161,224		6,238	613,299
-2		16,342	30,468	8,312		514		36,303		1,338	93,277
-1		17,389	16,919	2,581		11,381	4,331	24,320		10,327	87,248
0										771	771
1		2,634	5,815			15,116	4,319	66,078		4,627	98,590
2											
3											
4											
5											
6											
7											
8											
9											
10											
11											
12											
13											
14											
15											
16											
17											
18											
合計	7,143	73,234	89,446	320,658	42,986	27,282	21,211	287,924	0	23,300	893,184

	合計	D 10	D 13	D 16	D 19	D 22	D 25	D 29	D 32	D 35	D 38	D 41	D 51
-3階 基礎	7,144		4,084	3,060									
-3階 柱	36,868	359	12,509	29	1,546	5,457	16,968						
-3階 壁	36,242	845	1,283		14,625	19,489							
-3階 基礎梁	309,766	62	50,239	110,930			28,413	120,122					
-3階 基礎小梁	42,983	70	5,882	70	67	510	155	36,229					
-3階 梁	270		81		189								
-3階 小梁	12,561		1,809					10,752					
-3階 床版	161,225	10,230	59,087	91,908									
-3階 雑	6,239	792	3,205		513	882		847					
-2階 柱	16,344		7,704	328		37	8,275						
-2階 壁	30,469	757	724	31	28,957								
-2階 基礎梁	8,313	228	2,963	251			4,871						
-2階 梁	515		359	156									
-2階 床版	36,302	5,268	29,679		1,355								
-2階 雑	1,338	325	1,013										
-1階 柱	17,391	1,416	6,929	39	2,801	526	5,680						
-1階 壁	16,921	1,494	7,688	3,497	3,858	384							
-1階 基礎梁	2,580	95	995				1,490						
-1階 梁	11,380	190	3,986	219			6,985						
-1階 小梁	4,331	139	1,340	222	73	2,557							
-1階 床版	24,320	3,234	20,599	181	306								
-1階 雑	10,328	383	2,022		7,531	332	60						
0階 雑	770	241	245	257		27							
1階 柱	2,632	703	1,375	554									
1階 壁	5,815	1,152	4,535	128									
1階 梁	15,115	423	4,921	175	348	541	8,707						

締日: 末日

出荷月	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
平成11年 6月	196	196											
平成11年 7月	51,977	439	10,321	41,217									
平成11年 8月	289,732	1,541	34,986	99,176	378	510	22,251	130,890					
平成11年 9月	203,163	7,306	73,188	60,525	2,911	7,217	15,349	36,667					
平成11年10月	21,250	2,126	11,115	5,048	366	1,894	701						
平成11年11月	26,866	255	5,632		7,112	7,679	6,188						
平成11年12月	64,827	5,489	35,187	467	8,321	9,038	6,325						
平成12年 1月	61,076	1,015	15,341	500	27,840	37	16,343						
平成12年 2月	34,686	4,563	22,949	270	2,986	2,583	942	393					
平成12年 3月	1,026	388	638										
平成12年 4月	52,474	2,697	15,233	2,574	25,238	721	6,011						
平成12年 5月	2,499	455	1,775			269							
平成12年 6月	71,066	2,797	26,728	2,088	27,801	4,158	7,494						
平成12年 7月	10,186	2,159	7,140	887									
平成12年 8月	2,158	703	1,140	315									
平成12年 9月	0												
平成12年10月	0												
平成12年11月	0												
平成12年12月	0												
平成13年 1月	0												
平成13年 2月	0												
平成13年 3月	0												
合計	893,182	32,129	261,373	213,067	102,953	34,106	81,604	167,950	0	0	0	0	0

ジエムビル付帯施設工 86-7

-3階床版 B北. B3F.S.



13

3500

18本

(3.5m- 18)

28

70-1 **ジェムビル付帯施設工**
1階基礎梁 A北,FG3,増打 9/18



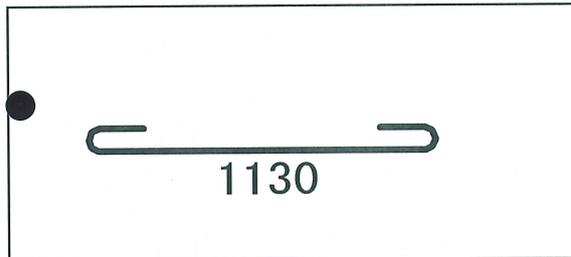
SD295A **D16** (3500mm (3.5m- 6)) **6本**

70-1 **ジェムビル付帯施設工**
1階基礎梁 A北,FG3,増打 9/18



SD295A **D16** (3500mm (3.5m- 6)) **6本**

1410_切 24_本 D16^{SD295A} 岸鉄
〈定尺 4.5m - 8本〉 249-1



ジェムビル付帯施設工
F工区. 柱寝巻き 8/28

日付	入荷	加工		出荷		摘要	出荷伝票番号		
		部位	定尺	実重	部位			定尺	実重
00/06/05	-1F床版		2,023	1,939	-1F床版	2,023	1,939	F工区.B1S F工区.B1S F工区.B1C F-B1C F-B1C.追加	197 198
	-1F柱		4,710	4,505	-1F柱	4,710	4,505	F工区.B1C F-B1C F-B1C.追加	195 196 199
	-1F雑		182	163	-1F雑	182	163	ゴミ置場.梁.補強 ゴミ置場.梁.補強	200
00/06/06	0F雑		257	257	0F雑	257	257	D16.生材 D16.生材	206
	1F梁		8,136	7,970	1F梁	8,136	7,970	F-1G F-1G.補強.追加工事 F-1G F-1G.補強.追加工事	201 202 203
00/06/09	-1F雑		7,770	7,521	-1F雑	7,770	7,521	F-B1W F-B1W	207 208
00/06/10	-1F壁		6,031	5,850	-1F壁	6,031	5,850	F-B1F.壁 F-B1F.壁	209 210 211
	-1F床版		124	110	-1F床版	124	110	F-B1S.取-フS F-B1S.取-フS	213
	0F雑		122	118	0F雑	122	118	雑.D13 雑.D13	212
00/06/15	-1F壁		1,849	1,751	-1F壁	1,849	1,751	E-B1W.ゴミ置場 E-B1W.ゴミ置場	214
	1F床版		3,957	3,939	1F床版	3,957	3,939	F-デッキS F-デッキS.立上り F-デッキS F-デッキS.立上り	215 216
00/06/16	0F雑		38	36	0F雑	38	36	ジベル筋 ジベル筋	220
	1F床版		19,843	19,649	1F床版	19,843	19,649	F-1F.取-フS.立上り F-1F.取-フS.立上り	F-1S F-1S追加 F-1S F-1S追加
00/06/19	1F床版		2,164	2,152	1F床版	2,164	2,152	F-1S F-1S	222
	1F梁		686	681	1F梁	686	681	F-1F梁増打追加 F-1F梁増打追加	223
00/06/26	1F小梁		4,096	4,004	1F小梁	4,096	4,004	F北工区.1B F北-1B F北工区.1B F北-1B	224 225 226
	1F梁		1,343	1,285	1F梁	1,343	1,285	F北.1G上増打.S段差 F北.1G上増打.S段差	227 228
00/06/27	1F小梁		225	214	1F小梁	225	214	F北.1F.B F北.1F.B	233
	1F床版		4,154	4,088	1F床版	4,154	4,088	F北.1S下 F北.1S下	229 230
	1F雑		222	201	1F雑	222	201	1S.追加 1S.追加	232
00/06/29	1F床版		3,129	3,115	1F床版	3,129	3,115	F北-1S上 F北-1S上	231

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
繰越	79,201	23,849	6,153	16,483	25,391	-1,107	7,140	1,292					
6月入荷													
6月加工定尺	71,061	2,795	26,723	2,086	27,804	4,159	7,494						
実重	69,550	2,737	25,999	2,052	27,374	4,094	7,293						
6月出荷定尺	71,061	2,795	26,723	2,086	27,804	4,159	7,494						
実重	69,550	2,737	25,999	2,052	27,374	4,094	7,293						
次月繰越	8,140	21,054	-20,570	14,397	-2,413	-5,266	-354	1,292					

入荷累計	886,985	50,127	230,722	226,261	100,542	28,841	81,250	169,242					
加工累計定尺	878,845	29,073	251,292	211,864	102,955	34,107	81,604	167,950					
実重	868,011	28,788	246,686	210,041	101,390	33,754	80,632	166,719					
出荷累計定尺	880,835	29,265	253,090	211,864	102,955	34,107	81,604	167,950					
実重	869,957	28,973	248,447	210,041	101,390	33,754	80,632	166,719					
在庫累計	8,140	21,054	-20,570	14,397	-2,413	-5,266	-354	1,292					

		合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
1:10/07/02	入荷	5,060					5,060							
2:10/07/02	入荷	5,496						5,496						
3:10/07/10	入荷	2,758				2,758								
4:10/07/21	入荷	17,399	17,399											
5:10/07/21	入荷	5,970						5,970						
6:10/07/21	入荷	25,320						25,320						
7:10/07/21	入荷	3,632							3,632					
1:10/07/02	OF													
2:10/07/02	OF 雑	56	56											
3:10/07/02	OF 雑	140	140											
4:10/07/02	-3F 床版	15,618	439	1,194	13,985									

		合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
	繰越	-71,835	600	-30,654	13,193	-5,168	-10,326	-37,140	-2,340					
	7月入荷	65,635	17,399			2,758	5,060	36,786	3,632					
	7月加工													
	7月出荷	15,814	635	1,194	13,985									
	次月繰越	-6,200	17,998	-30,654	13,193	-2,410	-5,266	-354	1,292					

	入荷累計	886,984	50,127	230,721	226,261	100,542	28,840	81,250	169,242					
	加工累計	893,184	32,128	261,375	213,068	102,952	34,107	81,604	167,950					
	出荷累計	893,184	32,128	261,375	213,068	102,952	34,107	81,604	167,950					
	在庫累計	-6,200	17,998	-30,654	13,193	-2,410	-5,266	-354	1,292					

2：上野台マンション

平成 12年 6月分 集計結果

[単位:kg]

平成 21年 1月 26日

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
繰越	225,526	64,493	80,960	-8,427	39,099	37,948	11,453						
6月入荷	13,134				4,666	4,468	4,000						
6月加工定尺	117,392	24,109	43,860	5,055	10,737	24,229	9,402						
実重	115,250	23,701	42,769	4,957	10,531	23,998	9,294						
6月出荷定尺	117,392	24,109	43,860	5,055	10,737	24,229	9,402						
実重	115,250	23,701	42,769	4,957	10,531	23,998	9,294						
次月繰越	121,268	40,384	37,100	-13,482	33,028	18,187	6,051						

入荷累計	374,002	91,224	162,096	5,603	46,749	44,862	23,468						
加工累計定尺	252,734	50,840	124,996	19,085	13,721	26,675	17,417						
実重	247,117	49,771	121,452	18,788	13,460	26,431	17,215						
出荷累計定尺	252,734	50,840	124,996	19,085	13,721	26,675	17,417						
実重	247,117	49,771	121,452	18,788	13,460	26,431	17,215						
在庫累計	121,268	40,384	37,100	-13,482	33,028	18,187	6,051						

3：池田町役場旧館建替工

平成 12年 6月分 集計結果

[単位:kg]

平成 21年 1月 26日

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
繰越	213,725	38,470	48,613	-558	32,319	40,172	50,922	3,083	704				
6月入荷	13,134				4,666	4,468	4,000						
6月加工定尺	90,874	19,248	40,074	1,238	905	280	26,689	1,702	738				
実重	89,356	18,963	39,231	1,219	904	271	26,343	1,702	723				
6月出荷定尺	90,874	19,248	40,074	1,238	905	280	26,689	1,702	738				
実重	89,356	18,963	39,231	1,219	904	271	26,343	1,702	723				
次月繰越	135,985	19,222	8,539	-1,796	36,080	44,360	28,233	1,381	-34				

入荷累計	466,345	80,854	146,954	13,652	38,209	44,640	137,198	4,134	704				
加工累計定尺	330,360	61,632	138,415	15,448	2,129	280	108,965	2,753	738				
実重	325,473	61,027	135,868	14,734	2,097	271	107,999	2,754	723				
出荷累計定尺	330,360	61,632	138,415	15,448	2,129	280	108,965	2,753	738				
実重	325,473	61,027	135,868	14,734	2,097	271	107,999	2,754	723				
在庫累計	135,985	19,222	8,539	-1,796	36,080	44,360	28,233	1,381	-34				

5：前川マンション新築

平成 12年 6月分 集計結果

[単位:kg]

平成 21年 1月 26日

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
繰越	53,328	7,752	29,369	501	487	3,942	11,277						
6月入荷													
6月加工定尺	48,202	5,798	24,933	3,777	223	2,112	11,359						
実重	46,986	5,602	24,112	3,699	217	2,070	11,286						
6月出荷定尺	48,202	5,798	24,933	3,777	223	2,112	11,359						
実重	46,986	5,602	24,112	3,699	217	2,070	11,286						
次月繰越	5,126	1,954	4,436	-3,276	264	1,830	-82						

入荷累計	142,064	13,404	66,719	15,261	5,360	9,281	32,039						
加工累計定尺	136,938	11,450	62,283	18,537	5,096	7,451	32,121						
実重	133,901	11,118	60,502	18,097	5,015	7,291	31,878						
出荷累計定尺	136,938	11,450	62,283	18,537	5,096	7,451	32,121						
実重	133,901	11,118	60,502	18,097	5,015	7,291	31,878						
在庫累計	5,126	1,954	4,436	-3,276	264	1,830	-82						

現場名	元 請	班	繰 越	当月入荷	当月加工		当月出荷		次月繰越	契約屯数	入荷累計	加工累計		出荷累計		在庫累計
					定尺重量	実寸重量	定尺重量	実寸重量				定尺重量	実寸重量	定尺重量	実寸重量	
2: 上野台マンション	大森建設	船場鉄筋	223,946	13,134	117,388	115,250	117,388	115,250	119,692	816,463	361,463	241,771	236,707	241,771	236,707	119,692
3: 池田町役場旧館建替工	大森建設	田中鉄筋	452,116	13,134					465,251	839,517	466,346	1,095	1,093	1,095	1,093	465,251
4: 山田地区集合住宅新築	小成組	田中鉄筋	194,795		109,237	107,003	109,237	107,003	85,558	1,492,471	1,020,822	935,264	917,155	928,187	910,135	85,558
5: 前川マンション新築	笹中工務店	山田鉄筋	53,328		48,204	46,986	38,292	37,362	5,124	225,600	142,064	136,940	133,900	127,028	124,276	5,124
8: 山田地区集合住宅新築	小成組	田中鉄筋	195,065		109,237	107,003	109,237	107,003	85,827		1,020,822	934,995	916,891	927,918	909,870	85,827
11: 箕面千里ハイツ	小成組	池田鉄筋	29,642		15,682	15,483	15,682	15,483	13,960		262,034	248,074	242,667	224,120	219,471	13,960
12: ジェムビル新築工事	笹中工務店	田中鉄筋	504,396		71,065	69,550	71,065	69,550	433,331	1,501,261	821,349	388,018	381,896	390,009	383,842	433,331
16: 石橋ハイツ	小成組	船場鉄筋	74,654	122,840					197,494		197,494					197,494
17: 山田電気(株)本社ビル	小成組	田中鉄筋	-14,282		19,243	19,126	19,243	19,126	-33,525		510,874	544,399	538,701	544,399	538,701	-33,525
合 計			1,713,659	149,108	490,056	480,400	480,144	470,776	1,372,711	4,875,312	4,803,268	3,430,556	3,369,011	3,384,527	3,324,095	1,372,711

	合計	D 1 0	D 1 3	D 1 6	D 1 9	D 2 2	D 2 5	D 2 9	D 3 2	D 3 5	D 3 8	D 4 1	D 5 1
6月入荷	149,108			23,165	22,680	44,819	58,445						
6月加工	490,056	116,614	162,813	23,761	38,986	44,652	62,269	40,173		390		399	
6月出荷	480,144	115,523	159,551	23,646	38,904	43,712	57,847	40,173		390		399	
